



S. No	4
Name of the work with location:	Link road from Garhi to Nonial
Department/Organization:	Health
Executive Agency	PWD (R&B) Div. Nowshera
Block/District:	Qila Darhal/Rajouri
AA Cost (Rs. In lakhs)	40.00
Total Cost of Completion/ Expenditure incurred ending 3/2022 (Rs. In lakhs)	36.00
Date of Start (Month/Year)	January, 2009
Date of Completion (Month/Year)	March, 2022
No. of Beneficiaries:	1500



S. No	5
Name of the work with location:	Constt. of 4 Sets of staff quarter at PHC Laroka (Double Story)
Department/Organization:	Health
Executive Agency	PWD (R&B) Div. Nowshera
Block/District:	Qila Darhal/Rajouri
AA Cost (Rs. In lakhs)	36.00
Total Cost of Completion/ Expenditure incurred ending 3/2022 (Rs. In lakhs)	
Date of Start (Month/Year)	December, 2015
Date of Completion (Month/Year)	March, 2022
No. of Beneficiaries:	1500




S. No	8
Name of the work with location:	Constt. Of 2-rooms School building at M/S Handan
Department/Organization:	Rural Dev. Deptt
Executive Agency	BDO Nowshera
Block/District:]	Nowshera/ Rajouri
AA Cost (Rs. In lakhs)	20.00
Total Cost of Completion/ Expenditure incurred ending 3/2022 (Rs. In lakhs)	19.94
Date of Start (Month/Year)	December, 2016
Date of Completion (Month/Year)	March, 2022
No. of Beneficiaries:	140



S. No	9
Name of the work with location:	Community Centre at Handan
Department/Organization:	Rural Dev. Deptt
Executive Agency	BDO Nowshera
Block/District:]	Nowshera/ Rajouri
AA Cost (Rs. In lakhs)	15.00
Total Cost of Completion/ Expenditure incurred ending 3/2022 (Rs. In lakhs)	14.67
Date of Start (Month/Year)	December, 2016

	Date of Completion (Month/Year)	March, 2022
	No. of Beneficiaries:	390

	S. No	17
	Name of the work with location:	Construction of two room school building at M/S Nonial
	Department/Organization:	Rural Dev. Deptt
	Executive Agency	BDO Nowshera
	Block/District:]	Nowshera/ Rajouri
	AA Cost (Rs. In lakhs)	20.00
	Total Cost of Completion/ Expenditure incurred ending 3/2022 (Rs. In lakhs)	19.97
	Date of Start (Month/Year)	December, 2016
	Date of Completion (Month/Year)	March, 2022
	No. of Beneficiaries:	132



Latitude: 33.31928
 Longitude: 74.242625
 Elevation: 896.1±14 m
 Accuracy: 2.4 m
 Azimuth: 74° (E)
 Pitch: -7.7° (2.8°)
 Time: 03-27-2022 12:31
 Note: Culvert at Sita Ram Mohalla Sasalkote


S. No	31
Name of the work with location:	Constt.of Culvert Sita Ram Sasalkote
Department/Organization:	Rural Dev. Deptt
Executive Agency	RDD
Block/District:]	Doongi/ Rajouri
AA Cost (Rs. In lakhs)	5.00
Total Cost of Completion/ Expenditure incurred ending 3/2022 (Rs. In lakhs)	4.00
Date of Start (Month/Year)	January, 2018
Date of Completion (Month/Year)	March, 2022
No. of Beneficiaries:	150




Latitude: 33.324306
 Longitude: 74.238771
 Elevation: 893.2±14 m
 Accuracy: 6.3 m
 Azimuth: 17° (N)
 Pitch: -14.4° (-3.4°)
 Time: 03-27-2022 12:52
 Note: Culvert ward no 6 and 7 at sasalkote


S. No	32
Name of the work with location:	Constt. of Culvert W. No. 06 & 07
Department/Organization:	Rural Dev. Deptt
Executive Agency	RDD
Block/District:	Doongi/ Rajouri
AA Cost (Rs. In lakhs)	10.00
Total Cost of Completion/ Expenditure incurred ending 3/2022 (Rs. In lakhs)	9.22
Date of Start (Month/Year)	January, 2018
Date of Completion (Month/Year)	March, 2022

	No. of Beneficiaries:	450
--	------------------------------	------------


	S. No	33
	Name of the work with location:	Constt. of Pond alongwith P/Work W.No.07 Sasalkote
	Department/Organization:	Rural Dev. Deptt
	Executive Agency	RDD
	Block/District:]	Doongi/ Rajouri
	AA Cost (Rs. In lakhs)	5.00
	Total Cost of Completion/ Expenditure incurred ending 3/2022 (Rs. In lakhs)	5.00
	Date of Start (Month/Year)	January, 2018
	Date of Completion (Month/Year)	March, 2022
	No. of Beneficiaries:	120


	S. No	35
	Name of the work with location:	Constt of Culvert at Sasalkote near Play Ground Sasalkote
	Department/Organization:	Rural Dev. Deptt
	Executive Agency	RDD
	Block/District:]	Doongi/ Rajouri
	AA Cost (Rs. In lakhs)	10.00
	Total Cost of Completion/ Expenditure incurred ending 3/2022	9.70

	(Rs. In lakhs)	
	Date of Start (Month/Year)	January, 2018
	Date of Completion (Month/Year)	March, 2022
	No. of Beneficiaries:	560


	S. No	12
	Name of the work with location:	Const. of road from Roshan Lal HO to Raj Kumar moh.
	Department/Organization:	Rural Dev. Deptt
	Executive Agency	BDO Nowshera
	Block/District:]	Nowshera/ Rajouri
	AA Cost (Rs. In lakhs)	2.50
	Total Cost of Completion/ Expenditure incurred ending 3/2022 (Rs. In lakhs)	2.50
	Date of Start (Month/Year)	January, 2016
	Date of Completion (Month/Year)	March, 2022

	No. of Beneficiaries:	450
--	------------------------------	------------

	S. No	14
	Name of the work with location:	Pacca lane, P/Path w. no. 3
	Department/Organization:	Rural Dev. Deptt
	Executive Agency	BDO Nowshera
	Block/District:]	Nowshera/ Rajouri
	AA Cost (Rs. In lakhs)	4.00
	Total Cost of Completion/ Expenditure incurred ending 3/2022 (Rs. In lakhs)	3.99
	Date of Start (Month/Year)	January, 2018
	Date of Completion (Month/Year)	March, 2022
No. of Beneficiaries:	100	

	S. No	13
	Name of the work with location:	Pacca lane, P/Path w. no. 2
	Department/Organization:	Rural Dev. Deptt
	Executive Agency	BDO Nowshera
	Block/District:]	Nowshera/ Rajouri
	AA Cost (Rs. In lakhs)	5.00
	Total Cost of Completion/ Expenditure incurred ending 3/2022 (Rs. In lakhs)	5.00
Date of Start (Month/Year)	January, 2018	

	Date of Completion (Month/Year)	March, 2022
	No. of Beneficiaries:	120

	S. No	26
	Name of the work with location:	Constt. Of Pacca path from Golden Brick Kilin Moh. To Shamshan Ghat Jameer Nalla
	Department/Organization:	Rural Dev. Deptt
	Executive Agency	BDO Nowshera
	Block/District:]	Nowshera/ Rajouri
	AA Cost (Rs. In lakhs)	3.00
	Total Cost of Completion/ Expenditure incurred ending 3/2022 (Rs. In lakhs)	2.28
	Date of Start (Month/Year)	December, 2017
	Date of Completion (Month/Year)	March, 2022
	No. of Beneficiaries:	90



S.NO	1
Name of the work with location	Construction of Badugam Dukran road (1.50 Km)
Department /Organization	PWD (R&B)
Executive Agency	Special Sub Division Gurez
Block/District	Tulail/Bandipora
AA Cost (Rs. in laks)	100.00
Total cost of completion /expenditure incurred ending 03/2022	90.00
Date of Start (Moth/Year)	06/2018
Date of completion (Month/Year)	03/2022
No of Beneficiaries	6000



Const. of Link road from culvert of S M Pura to Jasso Chak Chamliyal

Sector : PWD, Samba

Date of commencement : 20216-2017


Date of Completion : 03/2022

Estimated Cost : 28.00 Lacs

Completion Cost : 27.55 Lacs

No. of souls benefitted : 800

Observation /recommendation of stakeholders: Better Accessibility

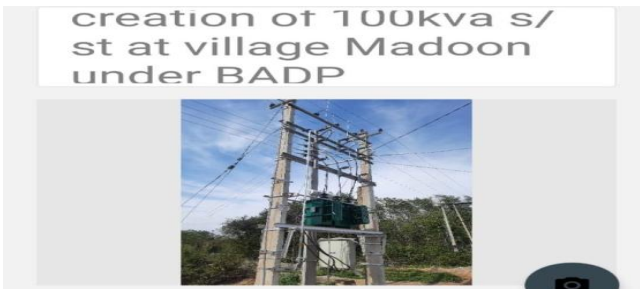

Creation of S/Stn. alongwith HT/LT Line at Madoon

Sector : PDD, Samba

Date of commencement : 2018-2019

Date of Completion : 01/2022

Estimated Cost : 6.10 Lacs

Completion Cost : 5.90 Lacs

No. of souls benefitted : 220

Observation /recommendation of stakeholders: : Infrastructure creation for Benefit of People.



Creation of S/Stn. alongwith HT/LT Line at Padri

Sector : PDD, Samba

Date of commencement : 2018-2019

Date of Completion : 03/2022

Estimated Cost : 3.35 Lacs

Completion Cost : 3.22 Lacs

No. of souls benefitted : 235

Observation/recommendation of stakeholders: Infrastructure creation for Benefit of People.



Creation of S/Stn. alongwith HT/LT Line at Sarwa

Sector : PDD, Samba

Date of commencement : 2018-2019

Date of Completion : 03/2022

Estimated Cost : 3.35 Lacs

Completion Cost : 3.22 Lacs

No. of souls benefitted : 260

Observation/recommendation of stakeholders: creation of Infrastructure for betterment of local people



Creation of S/Stn. alongwith HT/LT Line at Manohar Gopala

Sector : PDD, Samba

Date of commencement : 2018-2019

Date of Completion : 03/2022

Estimated Cost : 4.10 Lacs

Completion Cost : 4.08 Lacs

No. of souls benefitted : 260

Observation /recommendation of stakeholders: Infrastructure creation for Benefit of People.



Shifting of HT/LT Line at Barota

Sector : PDD, Samba

Date of commencement : 2018-2019

Date of Completion : 03/2022

Estimated Cost : 6.98 Lacs

Completion Cost : 6.89 Lacs

No. of souls benefitted : 290

Observation /recommendation of stakeholders: On the peoples demand HT line is shifted for safety of local people



Link road to village Reyian

Sector : PWD, Samba

Date of commencement : 2017-2018

Date of Completion : Physically Complete

Estimated Cost : 45.00 Lacs

Expenditure: 20.86Lacs

No. of souls benefitted : 750

Observation /recommendation of stakeholders: Better connectivity



Renovation of CFC at Kullian , Sadoh

Sector : Rural Development Department

Date of commencement : 10.02.2020

Date of Completion : 03/2022

Estimated Cost : 5.00 Lacs

Completion Cost : 4.73 Lacs

No. of souls benefitted : 70

Observation /recommendation of stakeholders: Facility for community of the area



Const. of Marriage Shed/Hall at Balode

Sector :RDD, Samba

Date of commencement : 2016-2017

Date of Completion : Completed

Estimated Cost : 8.00 Lacs

Expenditure: 4.81 Lacs


No. of souls benefitted : 500

Observation /recommendation of stakeholders: Community Asset




BADP

R&B Division Kathua



Name of the project : Const. of road from Jaymal chak to house of Harman Singh Haria chak

others Sector :- BADP
Date of Commencement :-2021-22
Date of completion :-2021-22
Estimated cost :- 9.81 Lacs
Completion Cost :- 9.55 Lacs
No of Souls benefitted :- 2000
Observation/Recommendation of stake Holders : Public of the area satisfied, feeling relief due to const. Of this road

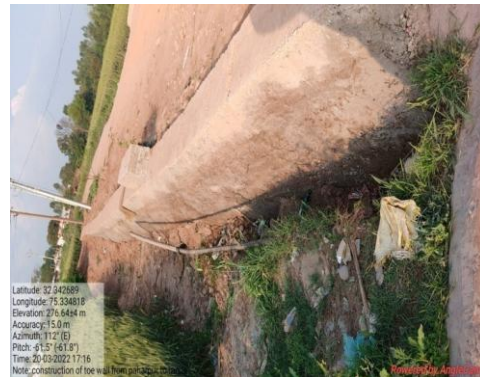

Name of the project : Const. of road Paharpur to village Mada

Sector :- BADP
Date of Commencement :-2021-22
Date of completion :-2021-22
Estimated cost :- 16.50 Lacs
Completion Cost :- 16.02Lacs
No of Souls benefitted :- 3000
Observation/Recommendation of stake Holders : Public of the area satisfied, feeling relief due to const. Of this road



Name of the project : Const. of Jawahar chak to Devo chak

others Sector :- BADP
Date of Commencement :-2021-22
Date of completion :-2021-22
Estimated cost :- 17.50 Lacs
Completion Cost :- 15.14 Lacs
No of Souls benefitted :- 1800
Observation/Recommendation of stake Holders : Public of the area satisfied, feeling relief due to const. Of this road

PRESENTATION FOR THE WORKS COMPLETED DURING THE YEAR 2021-22 IN RESPECT OF IRRIGATION DIVISION KATHUA

1



Improvement of Chhan Lal Din I&II.

Sector:- BADP

Date of Commencement: 2015-16

Date of Completion; March 2022

Estimated Cost: 12.40 Lacs

Completion Cost: 12.05 Lacs

No. of Souls benefited: 19 Nos. farmer benefitted

Observation/ recommendation of stakeholders: Construction of irrigation network for farmers.



Improvement of Hari Pur Saini.

Sector:- BADP

Date of Commencement: 2016-17

Date of Completion; March 2022

Estimated Cost: 12.00 Lacs

Completion Cost: 11.63 Lacs

No. of Souls benefited: 16 Nos. farmer benefitted

Observation/ recommendation of stakeholders: Construction of irrigation network for farmers.



Improvement of Hari Pur Saini.

Sector:- BADP

Date of Commencement: 2016-17

Date of Completion; March 2022

Estimated Cost: 12.00 Lacs

Completion Cost: 11.63 Lacs

No. of Souls benefited: 16 Nos. farmer benefitted

Observation/ recommendation of stakeholders: Construction of irrigation network for farmers.



Improvement of Rumbli Wali Khul

Sector:- District Sector

Date of Commencement: 2017-18

Date of Completion; March 2022

Estimated Cost: 3.60 Lacs

Completion Cost: 3.27 Lacs

No. of Souls benefited:: 7 Nos. farmer benefitted

Observation/ recommendation of stakeholders: Construction of irrigation network for farmers.



Improvement of Patti Wali Khul.

Sector:- BADP

Date of Commencement: 2017-18

Date of Completion; March 2022

Estimated Cost: 5.80 Lacs

Completion Cost: 5.34 Lacs

No. of Souls benefited: 11 Nos. farmer benefitted

Observation/ recommendation of stakeholders: Construction of irrigation network for farmers.



Improvement of Dhamni Khul.

Sector:- BADP

Date of Commencement: 2011-12

Date of Completion; March 2022

Estimated Cost: 27.60 Lacs

Completion Cost: 27.04 Lacs

No. of Souls benefited: 57 Nos. farmer benefitted

Observation/ recommendation of stakeholders: Construction of irrigation network for farmers.



Improvement of Dhamni Khul.

Sector:- BADP

Date of Commencement: 2011-12

Date of Completion; March 2022

Estimated Cost: 27.60 Lacs

Completion Cost: 27.04 Lacs

No. of Souls benefited: 57 Nos. farmer benefitted

Observation/ recommendation of stakeholders: Construction of irrigation network for farmers.

- Regards from
- Executive Engineer
- Irrigation Division
- Kathua

\

Photographs with required details of Completed works under BADP ST of Block Handwara




Sr.No	1
Name of work with Location	Dev of inner links at Khatana Mohala Nabadzab
Department/Organization	RDD
Executing Agency	RDD
Block	Handwara
AA cost (Rs in Lakhs)	7.736
Total cost of Completion/Expenditure incurred ending 03/2022	7.728
Date of Start (Month/Year)	09/2020
Date of Completion (Month/year)	06/2021
No of Beneficiaries	540

Photographs with required details of Completed works under BADP ST of Block Handwara




Sr.No	2
Name of work with Location	Dev of Inner links Bajard Mohala & Jatyal Mohala Nagranar
Department/Organization	RDD
Executing Agency	RDD
Block	Handwara
AA cost (Rs in Lakhs)	7.955
Total cost of Completion/Expenditure incurred ending 03/2022	7.954
Date of Start (Month/Year)	09/2020
Date of Completion (Month/year)	06/2021
No of Beneficiaries	580

Photographs with required details of Completed works underBADP Nornal of Block Qadirabad

	Sr.No	3
	Name of work with Location	Const of P/bund near Land of GH Ahmad Shiekh at Ward No 7 Gulgam C
	Department/Organization	RDD
	Executing Agency	RDD
	Block	Qadirabad
	AA cost (Rs in Lakhs)	5.14
	Total cost of Completion/Expenditure incurred ending 03/2022	4.87
	Date of Start (Month/Year)	01/03/20216
	Date of Completion (Month/year)	08-03-2021
	No of Beneficiaries	40

Photographs with required details of Completed works underBADP Nornal of Block Qadirabad

	Sr.No	4
	Name of work with Location	Const of P/bund near Land of Mohd Abdullah Lone at Herri Payeen
	Department/Organization	RDD
	Executing Agency	RDD
	Block	Qadirabad
	AA cost (Rs in Lakhs)	4.98
	Total cost of Completion/Expenditure incurred ending 03/2022	4.91
	Date of Start (Month/Year)	10-03-2016
	Date of Completion (Month/year)	28-08-2018
	No of Beneficiaries	45


Photographs with required details of Completed works under BADP of Block Qadirabad	
	Sr.No 5 Name of work with Location Const of P/bund near Land of Mohd Asraf Lone at Sky Touch School Herri payeen Department/Organization RDD Executing Agency RDD Block Qadirabad AA cost (Rs in Lakhs) 4.96 Total cost of Completion/Expenditure incurred ending 03/2022 4.94 Date of Start (Month/Year) 10-03-2016 Date of Completion (Month/year) 29-03-2018 No of Beneficiaries 40

Photographs with required details of Completed works under BADP of Block Tarathpora	
	Sr.No 6 Name of the work with location:- Const of /road from G Road from Sochalayri Bala Department/Organization RDD Executing Agency RDD Block/District/Scheme Tarathpora/ Kupwara/BADP(ST) AA cost (Rs.in Lakhs) 10 Allocated cost (Rs.in Lakhs) 0 Total Cost of Completion/Expenditure incurred ending 3/2022 8.87 Date of Start (Month/Year) 23/03/2018 Date of completion (Month/Year) Mar-22 No of Beneficiaries 40


**GEO-TAGGED PHOTOGRAPHS OF WORKS UNDER BADP CONVERGENCE OF BLOCK WAVOORA
FOR THE YEAR 2021-22**




S.No	07
Name of the work with location: -Const. of culvert at Kukar Kul NLO Gh Nabi Mughal Kawari	
Department/organization	RDD
Executing Agency	RDD
Block/District/Scheme	Wavooru/ Kupwara/BADP
A.A cost (Rs.in Lakhs)	2.0
Total Cost of Completion/Expenditure incurred ending 3/2022	1.954
Date of Start (Month/Year)	02-2020
Date of completion (Month/Year)	03-2020
No. of beneficiaries	195

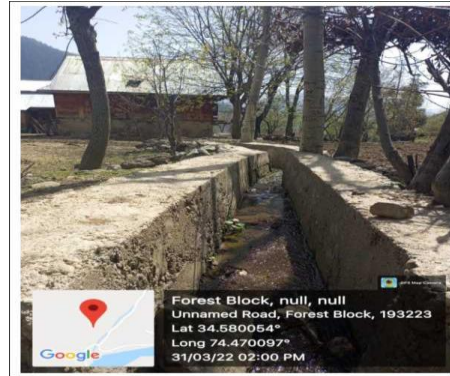

S.No	08
Name of the work with location: -Const. of Kul from Khatana Mohalla to Sarpanch Mohalla PMGSY road under BADP convergence	
Department/organization	RDD
Executing Agency	RDD
Block/District/Scheme	Wavooru/ Kupwara/BADP
A.A cost (Rs.in Lakhs)	2.0
Total Cost of Completion/Expenditure incurred ending 3/2022	2.0
Date of Start (Month/Year)	06-2019
Date of completion (Month/Year)	10-2019
No. of beneficiaries	18

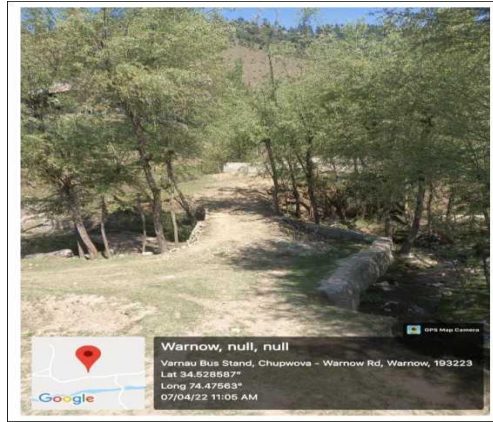

S.No	09
Name of the work with location: -Const. of Link Road NLO Mohd Maqbool to Ziyarat Shareef Warnow B	
Department/organization	RDD
Executing Agency	RDD
Block/District/Scheme	Wavoora/ Kupwara/BADP
A.A cost (Rs.in Lakhs)	3.05
Total Cost of Completion/Expenditure incurred ending 3/2022	2.98
Date of Start (Month/Year)	12-2019
Date of completion (Month/Year)	01-2020
No. of beneficiaries	230

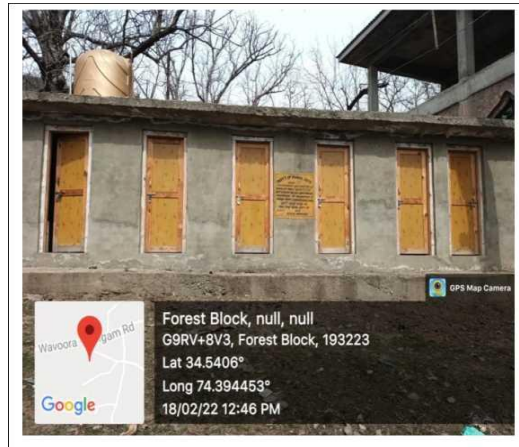

S.No	10
Name of the work with location: -Const. of Bathroom Nr old Jamia Masjid Maidanpora	
Department/organization	RDD
Executing Agency	RDD
Block/District/Scheme	Wavoora/ Kupwara/BADP
A.A cost (Rs.in Lakhs)	2.0
Total Cost of Completion/Expenditure incurred ending 3/2022	2.0
Date of Start (Month/Year)	12-2019
Date of completion (Month/Year)	03-2020
No. of beneficiaries	320

Photographs with required details of Completed works under BADP of Block Kalaroose



Dab Bal, null, null
H8FG+FG9, Dab Bal, 193222
Lat 34.673282°
Long 74.324104°
10/03/22 11:59 AM

Sr.No	11
Name of work with Location	Const. of Road From Main Road to Ab Ahad Malik At Lastiyal
Department/Organization	RDD
Executing Agency	RDD
Block	Kalaroose
AA cost (Rs in Lakhs)	2.00
Total cost of Completion/Expenditure incurred ending 03/2022	1.80
Date of Start (Month/Year)	10-03-2018
Date of Completion (Month/year)	29-03-2018
No of Beneficiaries	25

Photographs with required details of Completed works under BADP of Block Drugmulla



*Latitude: 34.602711
*Longitude: 74.283965
*Elevation: 1709.11517 m
*Accuracy: 2.3 m
*Azimuth: 199.133
*Pitch: -19.6°
*Time: 24.02.2022 12:35
*Date: const of p.Bund with drain NLO Jameela D/o Gh. Nabi Khayal Muqam-i-Shahwali

Sr.No	12
Name of work with Location	Const.of P.Bund with drain NLO Jameela D/o Gh. Nabi Khayal Muqam-i-Shahwali
Department/Organization	RDD
Executing Agency	RDD
Block	Drugmulla
AA cost (Rs in Lakhs)	2.00
Total cost of Completion/Expenditure incurred ending 03/2022	1.90
Date of Start (Month/Year)	01-2019
Date of Completion (Month/year)	29-03-2018
No of Beneficiaries	30

Photographs with required details of Completed works under BADP of Block Drugmulla



Latitude: 24.668
Longitude: 74.280333
Elevation: 638.33497 m
Accuracy: 5.2 m
Address: 52, ID
Pitch: -16.4
Time: 09-03-2022 03:16
Note: Fencing around panchayat ghar Drugmulla

Sr.No	13
Name of work with Location	Const. of fencing Panchayat Ghar Bramrie B
Department/Organization	RDD
Executing Agency	RDD
Block	Drugmulla
AA cost (Rs in Lakhs)	4.98
Total cost of Completion/Expenditure incurred ending 03/2022	4.86
Date of Start (Month/Year)	03-2016
Date of Completion (Month/year)	3/2022
No of Beneficiaries	80


Photographs with required details of Completed works under BADP of Block Wavoora



Forest Block, null, null
Unnamed Road, Forest Block, 193223
Lat 34.521425°
Long 74.479537°
15/04/22 12:51 PM

Sr.No	14
Name of work with Location	Const. of crossing Middle School ophen Phase II
Department/Organization	RDD
Executing Agency	RDD
Block	Wavoora/ Kupwara/BADP
AA cost (Rs in Lakhs)	17.95
Total cost of Completion/Expenditure incurred ending 03/2022	14.355
Date of Start (Month/Year)	03-2019
Date of Completion (Month/year)	08-2020
No of Beneficiaries	450

Photographs with required details of Completed works under BADP of Block Drugmulla

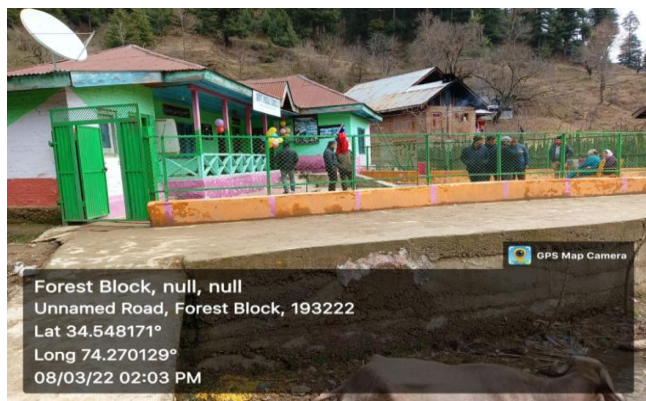

Sr.No	15
Name of work with Location	Const of Fencing around Middle School Zangli
Department/Organization	RDD
Executing Agency	RDD
Block	Hyhama
AA cost (Rs in Lakhs)	5.00
Total cost of Completion/Expenditure incurred ending 03/2022	4.50
Date of Start (Month/Year)	06-2020
Date of Completion (Month/year)	3/2022
No of Beneficiaries	80

Photographs with required details of Completed works under BADP of Block Wavoora



Sr.No	16
Name of work with Location	Const of Crossing near Hajam Mohalla Chart
Department/Organization	RDD
Executing Agency	RDD
Block	Hyhama
AA cost (Rs in Lakhs)	10.45
Total cost of Completion/Expenditure incurred ending 03/2022	8.89
Date of Start (Month/Year)	07-2012
Date of Completion (Month/year)	03-2020
No of Beneficiaries	14500

Subject: - Photographs of completed works with their description



Latitude: 34.079096
 Longitude: 74.205754
 Elevation: 1893.73±25 m
 Accuracy: 5.9 m
 Azimuth: 108° (E)
 Pitch: -7.1° (2.1°)
 Time: 11-09-2021 15:28
 Note: Doodra darakunjan road wBM grade ist khak bajri over grade ist



Latitude: 34.079317
 Longitude: 74.211708
 Elevation: 1963.51±69 m
 Accuracy: 5.1 m
 Azimuth: 263° (W)
 Pitch: -7.0° (3.6°)
 Time: 09-15-2021 12:59
 Note: doodran Darakunjan road in progress

Name of work with location	Const./upgrd. Of road from PMGSY Dudran road to Darakunjan (ST Road PLAN)
Department / Organization	R&B
Executive Agency	R&B
Block/ District	Boniyar/ Baramulla
AA Cost (Rs. In Lakhs)	184.00 lakh
Total Cost of competition/ Expenditure incurred ending 03/2022	103.91 Lakh
Year of start	2019
Year of completion	2021
No. of beneficiaries	500 souls



Name of work with location
Const. of culvert , lanes, Drains at various spots of village Binner, Shutloo, Venkara, Chakloo

Department / Organization
RDD

Executive Agency
RDD
Nadihal/Baramulla

Block/ District

AA Cost (Rs. In Lakhs)
6.20

Total Cost of competition/ Expenditure incurred ending 03/2022
3.89

Year of start
2019

Year of completion
2021

No. of beneficiaries
600

